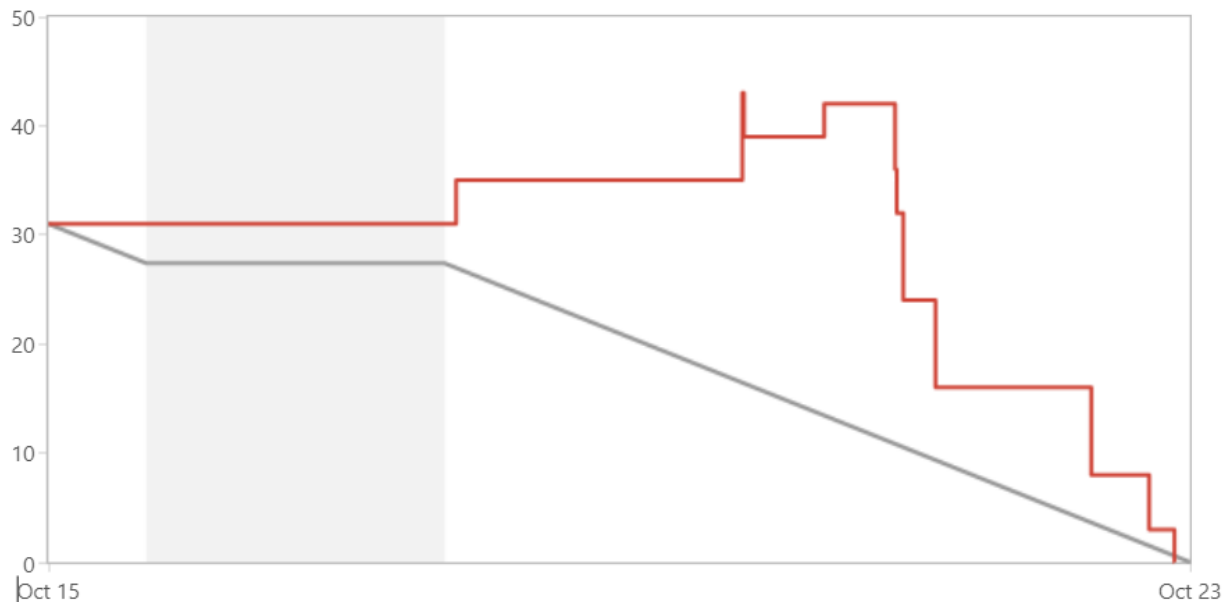Sprint 2 burndown chart: GMT-8-GANG

Status Report

For sprint 2, the burndown chart had increased in points to accommodate more tasks. These tasks were mostly project related such as preparing for demo, and adding necessary documentation, and we think this was necessary to assign people these tasks and get them recorded on Jira. There were some issues at the start of the sprint, but a lot of subtasks had to be done in sequence from the same user story to get it fully completed. We finished user stories about 4 days before the deadline and that was what we expected from this sprint. Since most progress was tracked by subtasks, this burndown chart is mostly what we expected from the beginning, where most of the individual user stories get completed in the second half of the sprint. The velocity of sprint 2 went as expected from what we learned from sprint 1. We decided to go with the same velocity from sprint 1 because we felt that it had a good pace and we expected the technical issues we faced from sprint 1 to not resurface for this sprint. We learned from sprint 1 that the pacing was good, but we need to keep the user stories more organized by using subtasks for this sprint, and everything worked out well and we finished all the user stories we targeted to complete for this sprint, as seen from the burndown chart.
